

2018 BOND UPDATE

BOND OVERSIGHT COMMITTEE MEETING MONDAY, MARCH 8, 2021

MASTER BUDGET SUMMARY

PROJECT	BEGINNING BUDGET	PROGRAM CONTINGENCY TRANSFERS	CURRENT BUDGET	COSTS AND COMMITMENTS	BALANCE
SMITHFIELD ELEMENTARY SCHOOL REPLACEMENT	\$28,165,000.00		\$28,165,000.00	\$27,336,069.74	\$828,930.26
HALTOM MIDDLE AND RICHLAND MIDDLE REPLACEMENTS	\$117,116,680.00		\$117,116,680.00	\$112,272,142.41	\$4,844,537.59
CHENEY HILLS ELEMENTARY AND PEDESTRIAN BRIDGE	\$34,051,913.00	\$440,383.00	\$34,492,296.00	\$34,241,766.64	\$250,529.36
SMITHFIELD MIDDLE SCHOOL GYM ADDITION	\$9,922,500.00		\$9,922,500.00	\$9,583,700.61	\$338,799.39
HVAC AND ROOFING	\$18,000,000.00		\$18,000,000.00	\$16,666,626.43	\$1,333,373.57
SECURE VESTIBULES AT VARIOUS SCHOOLS	\$2,126,257.00	\$1,762,653.00	\$3,888,910.00	\$3,829,926.83	\$58,983.17
HIGH SCHOOL AUDITORIUM UPGRADES	\$2,268,035.00		\$2,268,035.00	\$2,222,200.88	\$45,834.12
COLLEGIATE ACADEMY OF BIRDVILLE	\$1,000,000.00		\$1,000,000.00	\$732,834.83	\$267,165.17
TOTALS	\$212,650,385.00	\$2,203,036.00	\$214,853,421.00	\$206,885,268.37	\$7,968,152.63
TECHNOLOGY	\$40,152,105.00				•


BEGINNING PROGRAM CONTINGENCY \$9,000,048.00
PROGRAM CONTINGENCY EXPENDITURES (\$2,203,036.00)
PROGRAM CONTINGENCY BALANCE \$6,797,012.00

GRAND TOTAL


COMPLETED PROJECTS

- Collegiate Academy of Birdville
- Security Vestibules at Multiple Schools
- Smithfield Middle School Gymnasium Addition
- North Ridge Middle School Kitchen Roofing
- Birdville High School Roofing

- COMPLETED PROJECTS (continued)
 - Grace E. Hardeman Elementary HVAC
 - W.T. Francisco Elementary HVAC
 - North Oaks Middle HVAC
 - Birdville High School Art Lab HVAC
 - Haltom High School Chiller Replacement

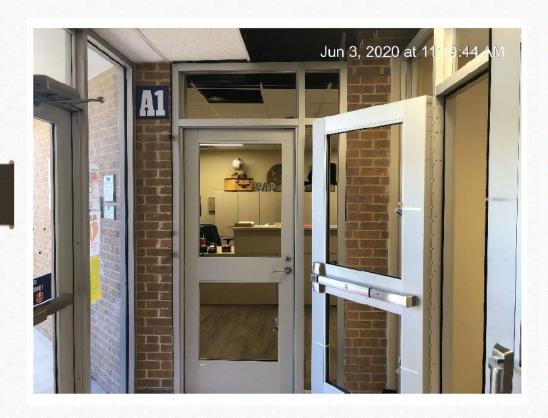



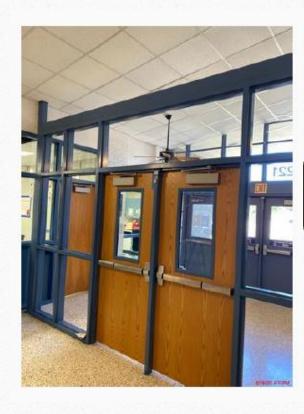


Security Vestibules at Multiple Schools



North Ridge Middle School Kitchen Roofing



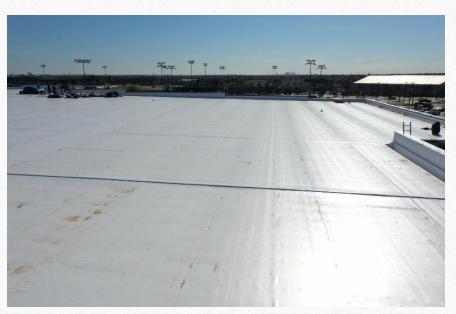

Birdville High School Roofing

SMITHFIELD MIDDLE SCHOOL GYM





- HVAC PROJECTS
 - Watauga Middle HVAC
 - In progress
 - Summer 2021 completion
 - Birdville High HVAC
 - In progress
 - Summer 2021 completion




- HALTOM AND RICHLAND MIDDLE SCHOOLS
 - Architect: PBK
 - Contractor: Adolphson and Peterson
 - Exterior masonry, roofing, and interior finishes in progress
 - ♦ On schedule
 - Summer 2021 completion



- CHENEY HILLS ELEMENTARY/PEDESTRIAN BRIDGE
 - Architect: VLK
 - Contractor: Ratcliff Constructors
 - Exterior masonry, roofing, and interior finishes in progress
 - Pedestrian Bridge fabrication in progress (March delivery)
 - Material delays due to COVID
 - Spring/summer 2021 completion

- SMITHFIELD ELEMENTARY SCHOOL
- HIGH SCHOOL AUDITORIUM UPGRADES
 - Architect: HKS
 - Exterior masonry, roofing, and interior finishes in progress
 - High School Auditorium Upgrades complete
 - Spring/Summer 2021 completion (Smithfield ES)


HIGH SCHOOL AUDITORIUM UPGRADES

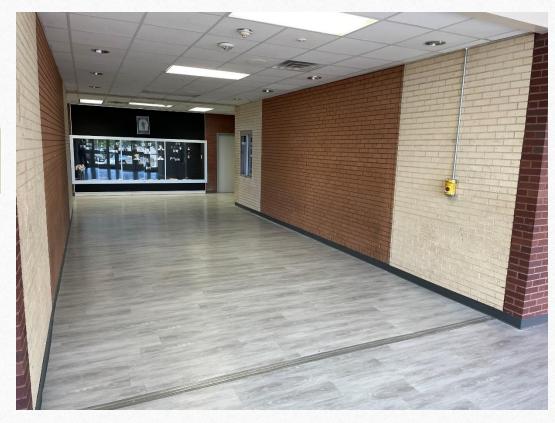

HALTOM HIGH LOBBY



HALTOM HIGH DRESSING ROOMS

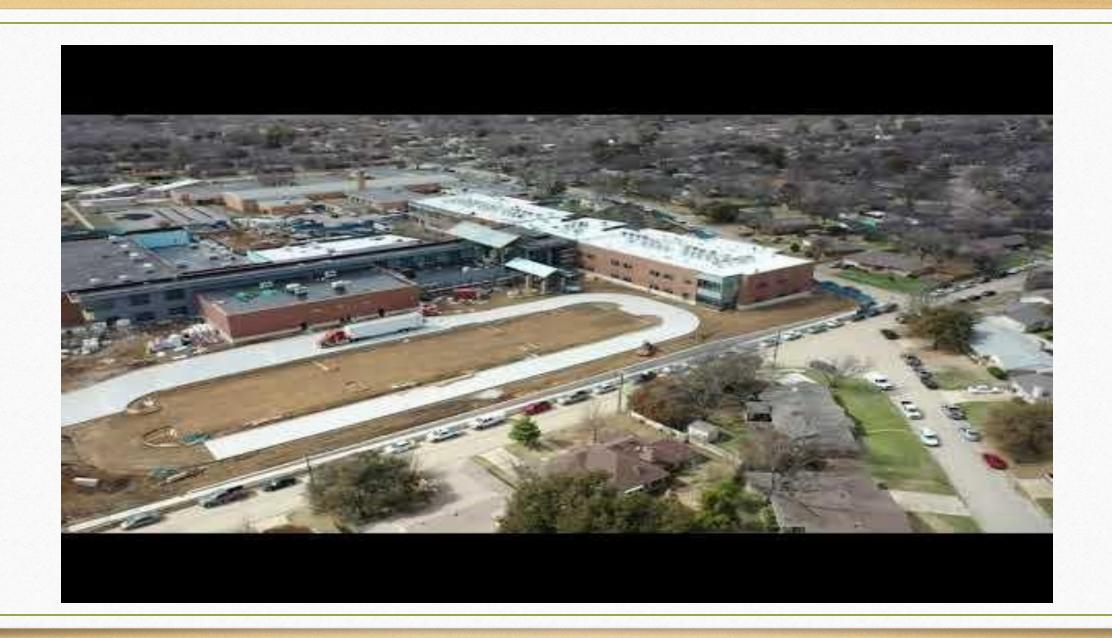

Birdville Independent School District
Birdville Independent School Dis

TECHNOLOGY UPDATE

BUDGET SUMMARY

PROJECT	BEGINNING BUDGET	COST AND COMMITMENTS	BALANCE	
Consolidated Security / Infrastructure	5,978,105	5,508,066	470,039	
Large Venue AV	649,000	317,667	331,333	
Projectors / Large Format Displays	3,000,000	540,464	2,459,536	
NOC / DR / Network	3,734,166	3,435,631	298,535	
Devices	26,790,834	11,192,065	15,598,769	
TOTALS	40,152,105	20,993,893	19,158,212	

In Procurement

Interactive flat panels for Pre-K-1st and Special Program classrooms at the two new elementary

campuses:

- 4k Ultra HD
- 50,000 hrs.
- 20 points of touch
- 65"



In Procurement

Large format displays for 2nd- through 5th-grade classrooms at the two new elementary campuses:

- 4k Ultra HD
- 65"
- Wall mounted



Projectors for new middle school classrooms:

- 120" screen
- Widescreen display
- Long lamp Life
- 4,000 lumens



Windows laptops for all campus and District

administrators:

- Touch screen
- i7 processors
- 16 GB memory
- 512 SSD hard drives
- Rollout late spring/early summer



Docking Stations:

- USB C
- Device charging
- Connect multiple monitors
- Windows & Chromebook devices
- Rollout late spring/early summer







New Phones:

- 7-inch capacitive touch screen
- Microsoft Teams-tailored user interface
- Districtwide rollout this summer





Datacenter:

- Cabling infrastructure
- Approved in Feb. 2021
- Install over next 6–8 weeks



Datacenter:

- Generator
- Approved in Feb. 2021
- Install over next 12–14 weeks
- Includes providing generator power to a war room



New Student Devices for 2021–22:

- 5th-grade
- 6th-grade
- 9th-grade



